

# City of Ladue Stormwater Project Status Report




Project Name: **Robin Hill Lane – McKnight Lane Bank Stabilization Project**  
Project Number: **1618**  
Project Phase: **Construction**  
Project Manager: **Mark Koester**  
**(314) 993-5665**  
[mkoester@cityofladue-mo.gov](mailto:mkoester@cityofladue-mo.gov)

## Scope:

*This project includes construction of approximately 840 lineal feet of storm channel renovation that includes bank stabilization, a triple box culvert, retaining walls, storm sewer adjustments, replacement of approximately 107 lineal feet of 18-inch diameter sanitary sewer to be installed in a casing, a prefabricated pedestrian bridge, landscape restoration, and appurtenances to be constructed in the Brookside, McKnight Lane and Robin Hill Subdivisions in the City of Ladue, Missouri.*

Estimated Project Value: **\$1.9 Million**

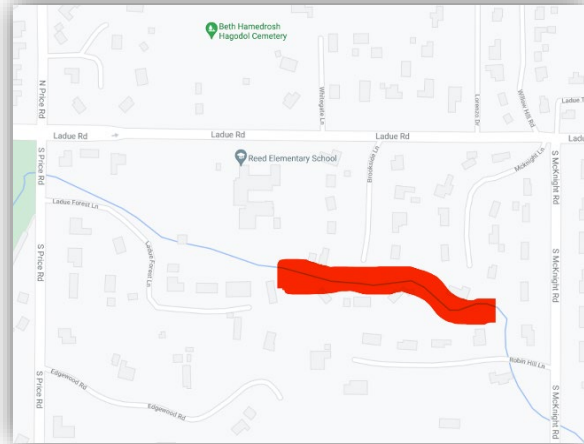

## Design Schedule

Design Start: **July 2018**  
Design Completion: **March 2021**

## Construction Schedule

Bid Opening Date: **April 15, 2021**  
Notice to Proceed Date: **May 11, 2021**  
Estimated Completion Date: **Spring 2022**

Design Professional: **Intuition & Logic, Inc.**

General Contractor: **Gershenson Construction**

## Status Update:

*Spire has relocated the gas main by extending the main from Ladue Forest Lane. Also, the sanitary sewer was extended across #5 Brookside Lane so that the #12 Brookside Lane lateral no longer crosses #5's property. With the resolution of these utility conflicts, Gershenson has installed the triple box culvert under Brookside Lane. Landscaping has been planted in areas that will not see any further construction. Work remains to be completed on the retaining walls that are upstream and downstream of the new box culvert. It is anticipated that construction may be completed before the end of Spring 2022, weather permitting.*

