

City of Ladue Stormwater Project Status Report




Project Name: **Robin Hill Lane – McKnight Lane Bank Stabilization Project**
Project Number: **1618**
Project Phase: **Construction**
Project Manager: **Mark Koester**
(314) 993-5665
mkoester@cityofladue-mo.gov

Scope:

This project includes construction of approximately 840 lineal feet of storm channel renovation that includes bank stabilization, a triple box culvert, retaining walls, storm sewer adjustments, replacement of approximately 107 lineal feet of 18-inch diameter sanitary sewer to be installed in a casing, a prefabricated pedestrian bridge, landscape restoration, and appurtenances to be constructed in the Brookside, McKnight Lane and Robin Hill Subdivisions in the City of Ladue, Missouri.

Estimated Project Value: **\$1.9 Million**

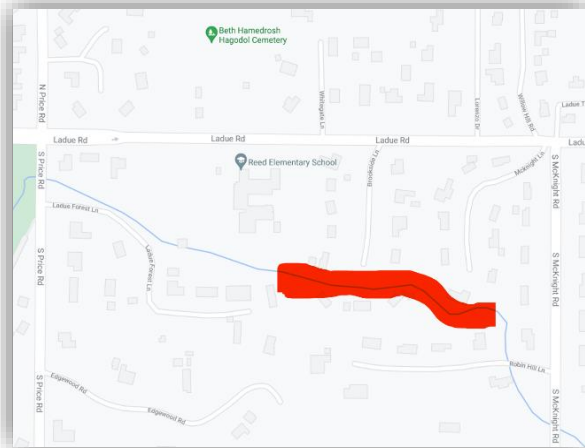

Design Schedule

Design Start: **July 2018**
Design Completion: **March 2021**

Construction Schedule

Bid Opening Date: **April 15, 2021**
Notice to Proceed Date: **May 11, 2021**
Estimated Completion Date: **October 2022**

Design Professional: **Intuition & Logic, Inc.**

General Contractor: **Gershenson Construction**

Status Update:

Construction has been delayed by Spire easement acquisition and gas main relocation. In the interim, Gershenson began construction on October 4, 2021 by starting at the downstream end of the project, and they are working upstream toward Brookside Lane.

