

City of Ladue Stormwater Project Status Report




Project Name: **Willow Hill Stormwater Infrastructure Project**
Project Number: **1614A**
Project Phase: **Construction**
Project Manager: **Amanda Griffin**
(314) 993-5665
agriffin@cityofladue-mo.gov

Scope:

This project includes construction of approximately 3,000 lineal feet of pipe sewers, varying in size from 12" to 42" in diameter and appurtenances that include pipe-in-tunnel, and roadway and landscape restoration to be constructed in the Willow Hill, Lorenzo Lane, and Loren Woods subdivisions in an area located north of Ladue Road and west of I-170, in the City of Ladue, Missouri.

Estimated Project Value: **\$2.9 Million**

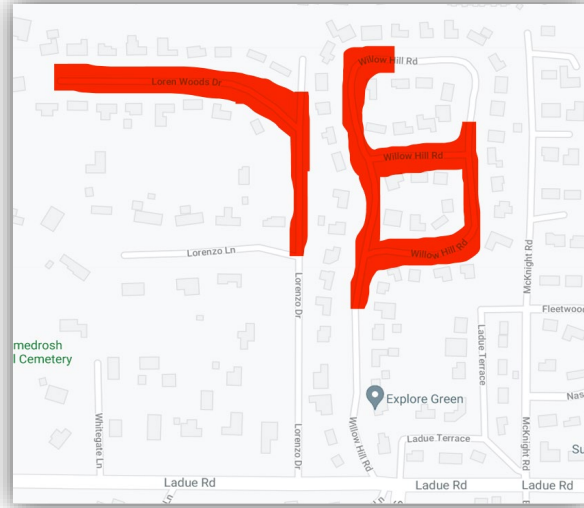

Design Schedule

Design Start: **July 2, 2018**
Design Completion: **April 2, 2021**

Design Professional: **HR Green**

Construction Schedule

Bid Opening Date: **May 6, 2021**
Notice to Proceed Date: **June 1, 2021**
Estimated Completion Date: **June 2022**

General Contractor: **Bi State Utilities Co.**

Status Update:

MAWC & Spire completed their utility relocation work. The contractor has begun the clearing, tree removal, and tree protection work. Pipe and materials have started to be delivered to the site.

