

# City of Ladue Stormwater Project Status Report



Project Name: **Willow Hill Stormwater Infrastructure Project**

Project Number: **1614A**


Project Phase: **Construction**

Project Manager: **Amanda Griffin**  
**(314) 993-5665**  
**agriffin@cityofladue-mo.gov**

## Scope:

*This project includes construction of approximately 3,000 lineal feet of pipe sewers, varying in size from 12" to 42" in diameter and appurtenances that include pipe-in-tunnel, and roadway and landscape restoration to be constructed in the Willow Hill, Lorenzo Lane, and Loren Woods subdivisions in an area located north of Ladue Road and west of I-170, in the City of Ladue, Missouri.*

Estimated Project Value: **\$2.9 Million**

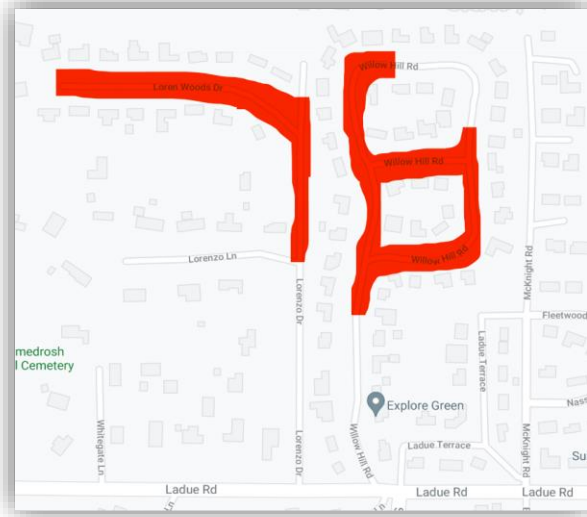

## Design Schedule

Design Start: **July 2018**  
Design Completion: **April 2021**

Design Professional: **HR Green**

## Construction Schedule

Bid Opening Date: **May 6, 2021**  
Notice to Proceed Date: **June 1, 2021**  
Estimated Completion Date: **June 2022**

General Contractor: **Bi State Utilities Co.**

## Status Update:

*Construction of the stormwater infrastructure is underway. Currently Bi-State's crew is installing pipe and a manhole structure in the roadway near #9 and #43 Willow Hill Road.*

